


CITY OF LONG BEACH - DEPARTMENT OF PUBLIC WORKS

PINE AVENUE IMPROVEMENT PROJECT / ANAHEIM STREET TO SEASIDE WAY

www.PineAveImprovement.com

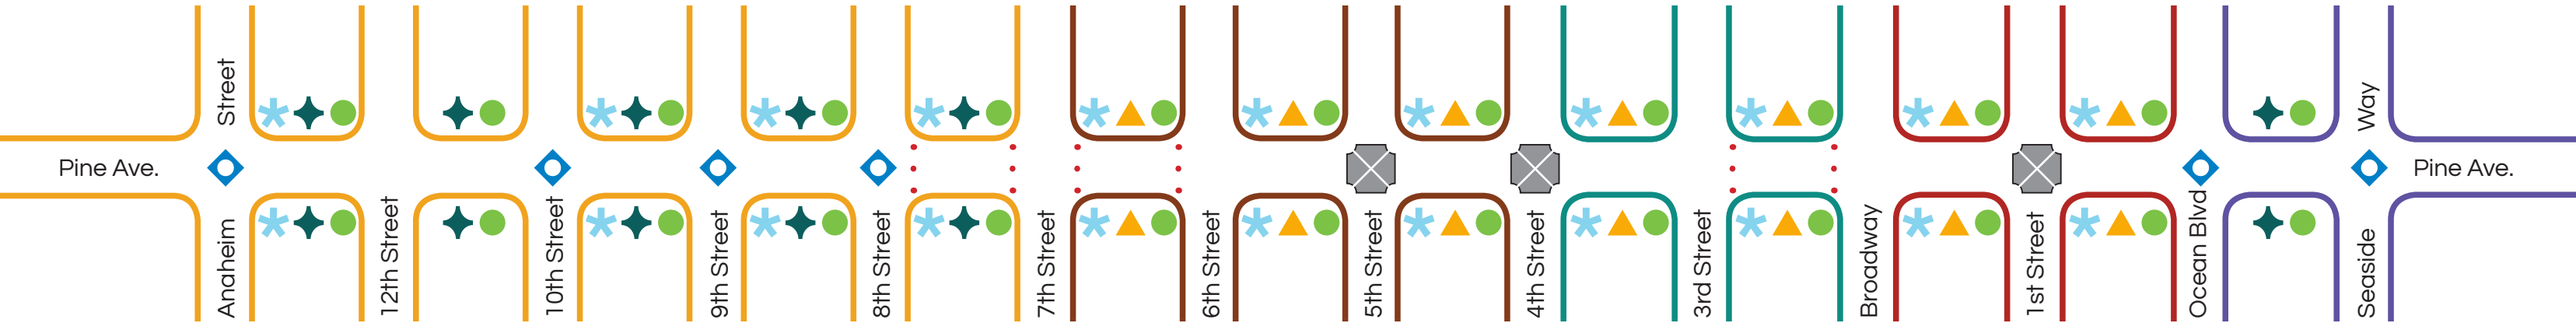

SEGMENT 1

1 Anaheim Street to 7th Street

APRIL 2014 - FEBRUARY 2015

ACTIVITY	IMPACT	DURATION
Potholing	Low	10 days
Tree Removal	Low	10 days
Bore/Trench	Med	20 days
Street Lights	Low	54 days
Traffic Signal	Med	75 days
Sidewalk/Curbs	Med	12 days
Landscape	Low	12 days
Paving	High	14 days
Loops/Striping	Med	10 days

SEGMENT 2

2 7th Street to 4th Street

JUNE 2014 - MARCH 2015

ACTIVITY	IMPACT	DURATION
Potholing	Low	3 days
Tree Removal	Low	7 days
Bore/Trench	Med	20 days
Street Lights	Low	3 days
Traffic Signal	Med	40 days
Sidewalk/Curbs	Med	10 days
Landscape	Low	15 days
Paving	High	12 days
Loops/Striping	Med	26 days

SEGMENT 3

3 4th Street to Broadway

SEPTEMBER 2014 - MARCH 2015

ACTIVITY	IMPACT	DURATION
Potholing	Low	10 days
Tree Removal	Low	7 days
Bore/Trench	Med	20 days
Street Lights	Low	13 days
Traffic Signal	Med	35 days
Sidewalk/Curbs	Med	21 days
Landscape	Low	24 days
Paving	High	10 days
Loops/Striping	Med	6 days

SEGMENT 4

4 Broadway to Ocean Boulevard

SEPTEMBER 2014 - APRIL 2015

ACTIVITY	IMPACT	DURATION
Potholing	Low	3 days
Tree Removal	Low	7 days
Bore/Trench	Med	24 days
Street Lights	Low	3 days
Traffic Signal	Med	23 days
Sidewalk/Curbs	Med	10 days
Landscape	Low	10 days
Paving	High	5 days
Loops/Striping	Med	7 days

SEGMENT 5

5 Ocean Boulevard to Seaside Way

APRIL 2015 - JULY 2015

ACTIVITY	IMPACT	DURATION
Potholing	Low	3 days
Storm Drain	Low	5 days
Bore/Trench	Med	8 days
Street Lights	Low	28 days
Traffic Signal	Med	22 days
Sidewalk/Curbs	Med	16 days
Landscape	Low	14 days
Paving	High	4 days
Loops/Striping	Med	7 days

- "Scramble" intersection
- Street tree planting
- Date palm planting at intersections
- New pedestrian lighting
- Refurbished pedestrian lighting
- Bollards
- Traffic Signal Modifications

- **IMPACT** relates to the estimated inconveniences (noise, street closures, etc.) caused by each activity.
- **DURATION** relates to the estimated total number of construction days each activity will take within each segment.
- Pedestrian access to all businesses will remain open during the entire project.

